EXHIBIT B - SCHEDULE

ID	Task Name	Duration	Start	Finish
1		180 days	Mon 5/6/13	Fri 11/1/13
2	NTP	1 day	Mon 5/6/13	Mon 5/6/13
3	Submittals	40 days	Mon 5/6/13	Fri 6/14/13
4	Material Delivery	50 days	Wed 6/5/13	Sun 8/4/13
5	Dewatering Install	14 days	Sat 6/15/13	Fri 6/28/13
6	Dewatering Drawdown (Initial)	20 days	Sat 6/29/13	Thu 7/18/13
7	Shafts for Vallarta	15 days	Fri 7/19/13	Fri 8/2/13
8	Jack pipe (1+46 to 11+63)	16 days	Sat 8/3/13	Sun 8/18/13
9	Open Cut to 15+00)	10 days	Fri 7/19/13	Sun 7/28/13
10	Shafts on Medianite	15 days	Wed 7/24/13	Wed 8/7/13
11	Casing (15+22 to 16+37)	10 days	Thu 8/8/13	Sat 8/17/13
12	Jack pipe o (15+00 to 17+96)	10 days	Sun 8/18/13	Tue 8/27/13
13	Manholes / Coatings	20 days	Mon 8/19/13	Sat 9/14/13
14	Pressure test joints	10 days	Wed 8/28/13	Fri 9/20/13
15	Mandrel / Deflection Test	5 days	Fri 9/27/13	Tue 10/1/13
16	Substantial Completion	1 day	Wed 10/2/13	Wed 10/2/13
17	Paving	15 days	Thu 10/3/13	Thu 10/17/13
18	Punchlist	29 days	Thu 10/3/13	Thu 10/31/13
19	Closeout Documents	29 days	Thu 10/3/13	Thu 10/31/13
20	Final Completion	1 day	Fri 11/1/13	Fri 11/1/13

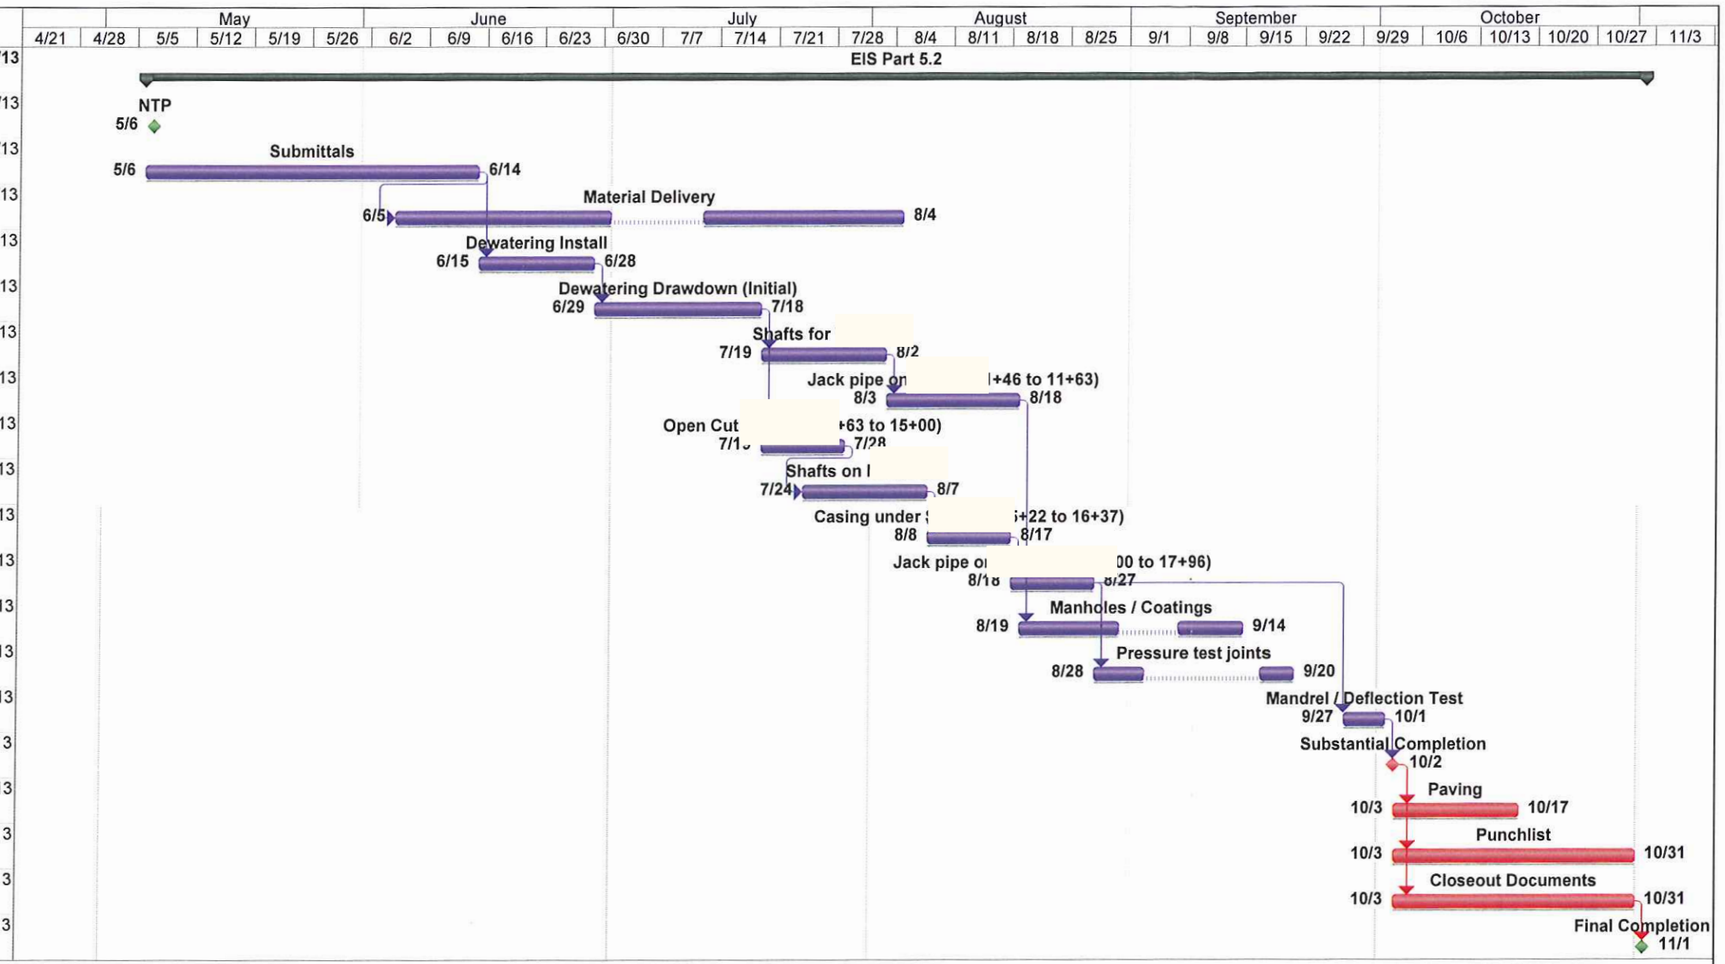

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone
